Prepared by: Kimley-Horn

Lincoln Park Pool Project Schedule

Updated: 9/26/2019

ID	Task Name	Duration	Start	Finish
1	Notice to Proceed	1 day	Tue 6/18/19	Tue 6/18/19
2	Task I - Project Management, Meetings and Coordination	497 days	Mon 6/24/19	Tue 5/18/21
3	**Task II - Master Plan Concept Development**	**70 days**	**Fri 6/28/19**	**Thu 10/3/19**
4	Kickoff / Stakeholder Meeting	1 day	Fri 6/28/19	Fri 6/28/19
5	Draft MP Concept	9 days	Fri 6/28/19	Wed 7/10/19
6	Submit Draft MP Concept	1 day	Wed 7/10/19	Wed 7/10/19
7	Review Meeting w/ County	51 days	Thu 7/11/19	Thu 9/19/19
8	Prepare Final MP	10 days	Fri 9/20/19	Thu 10/3/19
9	Task III - Topographic Survey	25 days	Mon 6/24/19	Fri 7/26/19
10	Task IV - Traffic Impact Statement (As Needed)	14 days	Fri 10/4/19	Wed 10/23/19
11	Task V - Engineering and Architectural Design and CDs	45 days	Fri 10/4/19	Thu 12/5/19
12	**Preliminary 30% Plans**	**82 days**	**Mon 9/30/19**	**Tue 1/21/20**
13	Site Civil	70 days	Mon 9/30/19	Fri 1/3/20
14	Landscape Architecture	70 days	Mon 9/30/19	Fri 1/3/20
15	Architecture	70 days	Mon 9/30/19	Fri 1/3/20
16	Aquatic Design	70 days	Mon 9/30/19	Fri 1/3/20
17	Submit to County for Review	11 days	Mon 1/6/20	Mon 1/20/20
18	30% Plan Review Meeting with County & CM	1 day	Tue 1/21/20	Tue 1/21/20
19	**Intermediate 60% Plans**	**44 days**	**Wed 1/22/20**	**Mon 3/23/20**
20	Site Civil	32 days	Wed 1/22/20	Thu 3/5/20
21	Landscape Architecture	32 days	Wed 1/22/20	Thu 3/5/20
22	Architecture	32 days	Wed 1/22/20	Thu 3/5/20
23	Aquatic Design	32 days	Wed 1/22/20	Thu 3/5/20
24	Submit to County for Review	10 days	Thu 3/5/20	Wed 3/18/20
25	60% Plan Review Meeting with County & CM	1 day	Mon 3/23/20	Mon 3/23/20
26	**Final 100% Plans**	**45 days**	**Tue 3/24/20**	**Mon 5/25/20**
27	Site Civil	35 days	Tue 3/24/20	Mon 5/11/20
28	Landscape Architecture	35 days	Tue 3/24/20	Mon 5/11/20
29	Architecture	35 days	Tue 3/24/20	Mon 5/11/20
30	Aquatic Design	35 days	Tue 3/24/20	Mon 5/11/20
31	Submit to County for Review	10 days	Mon 5/11/20	Fri 5/22/20
32	100% Plan Review Meeting with County & CM	1 day	Mon 5/25/20	Mon 5/25/20
33	**Task VI - Permitting Services**	**53 days**	**Mon 2/24/20**	**Wed 5/6/20**
34	City of Palmetto	53 days	Mon 2/24/20	Wed 5/6/20
35	SWFWMD	42 days	Mon 2/24/20	Tue 4/21/20
36	Manatee County	33 days	Thu 3/5/20	Mon 4/20/20
37	FDEP	13 days	Mon 4/6/20	Wed 4/22/20
38	Task VII - Bidding & Construction Phase Services	64 days	Mon 5/25/20	Thu 8/20/20
39	Construction Manager - PreConstruction Services	189 days	Mon 1/6/20	Thu 9/24/20
40	Bidding	90 days	Mon 5/25/20	Fri 9/25/20
41	Construction - Estimated Days	238 days	Mon 9/28/20	Wed 8/25/21

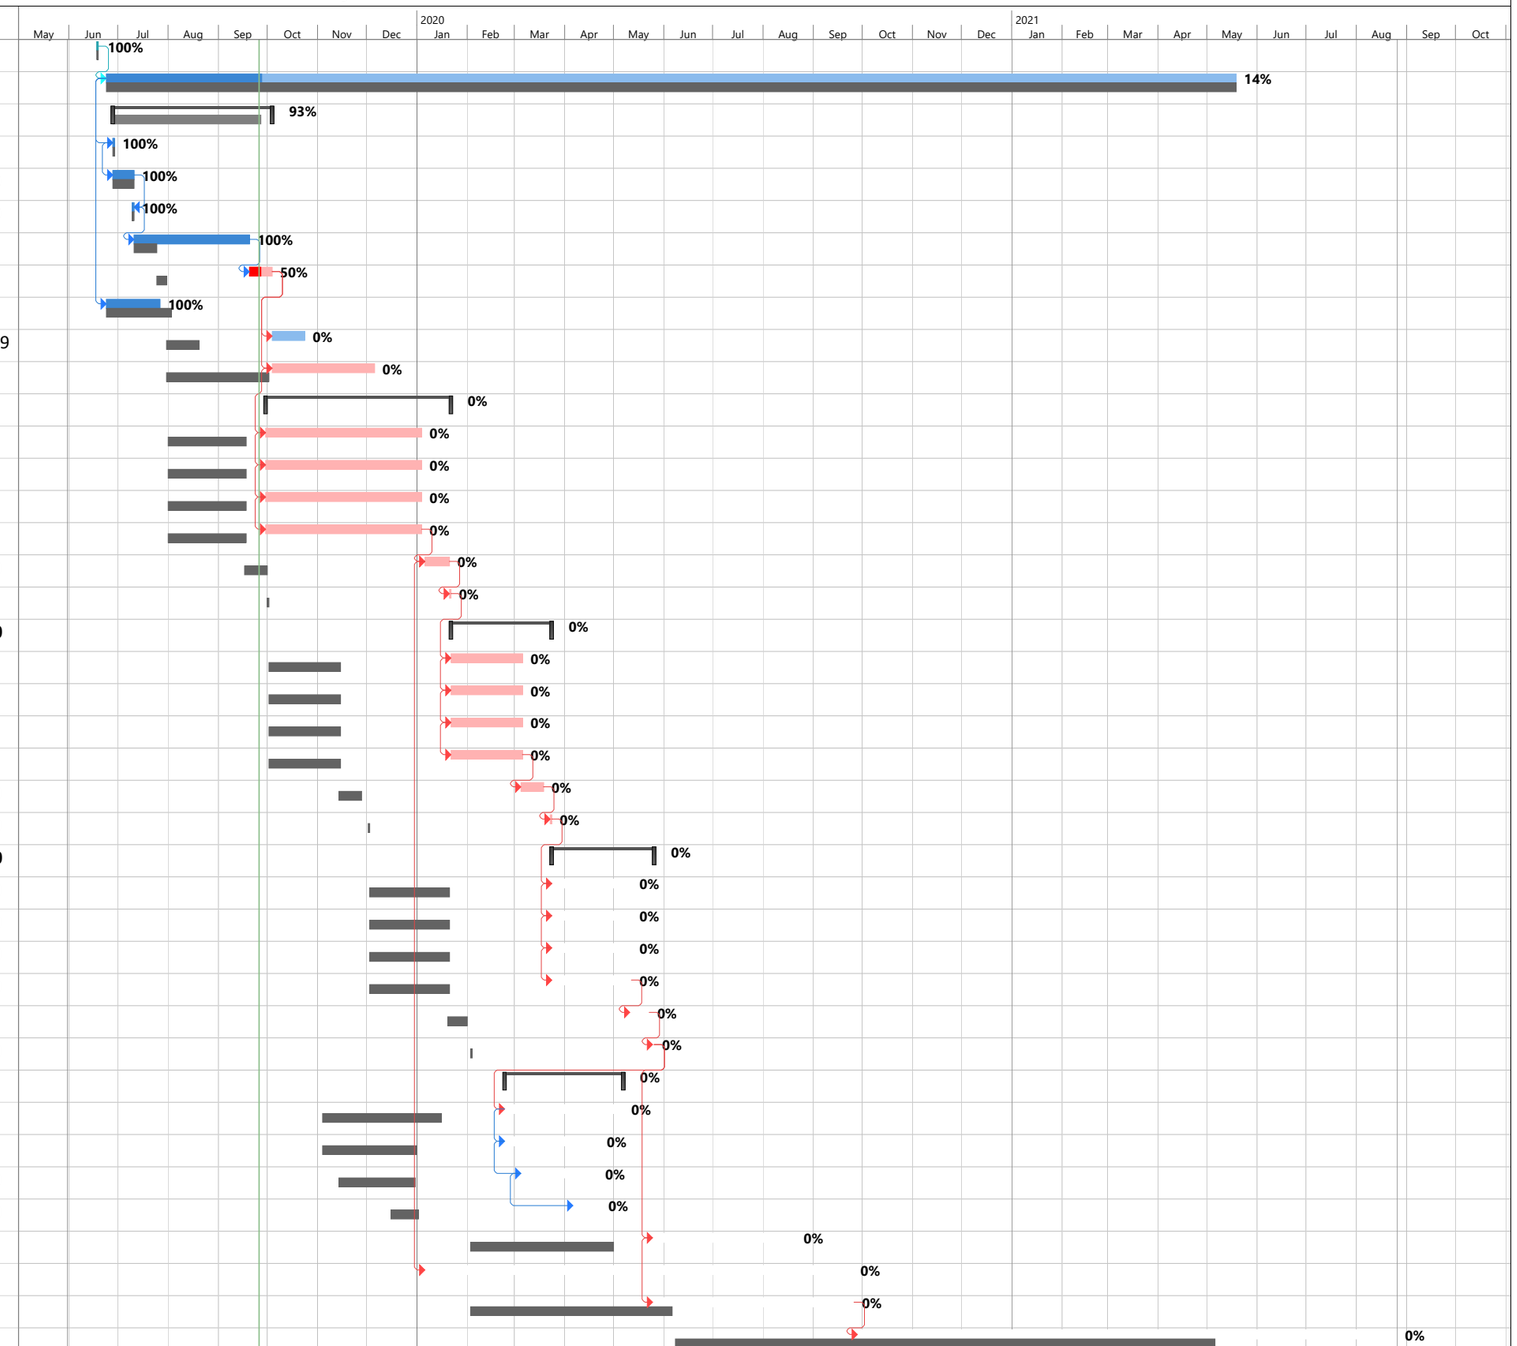
2020
2021
May Jun Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct
100%
14%
93%
100%
100%
100%
100%
50%
100%
0%
0%
0
